

Software Project Management Plan

for

Undergraduate Transfer Management System

Prepared by

Group 12

14.12.2025

Table of Contents

1	Overview	3
1.1	Purpose, scope, and objectives	3
1.2	Assumptions and constraints	4
1.3	Project deliverables	5
1.4	Schedule and budget summary	7
2	References	7
3	Definitions	8
4	Project context.....	9
4.1	Product acceptance plan	9
4.1.1	Acceptance Criteria	9
4.1.2	Acceptance Methods	10
4.1.3	Acceptance Process.....	10
4.2	Project organization	11
4.2.1	External interfaces	11
4.2.2	Internal structure	12
4.2.3	Roles and responsibilities.....	14
5	Project planning	15
5.1	Project work plans	15
5.1.1	Work activities.....	15
5.1.2	Schedule Allocation.....	22
5.1.3	Resource allocation	27
5.1.4	Budget allocation	28
5.1.5	Communications plan	29
5.2	Project assessment and control	29
5.2.1	Schedule control plan.....	29
5.2.2	Budget control plan.....	30
6	Product delivery	30
6.1	Delivery Approach	30
6.2	Information Flow During Delivery	31
6.3	Packaging and Delivery Method.....	31
6.3.1	Software Delivery	31
6.3.2	Source Code Delivery	31

6.3.3	Documentation Delivery	31
6.4	Delivered Artifacts.....	32
6.5	Acceptance and Handover.....	32
6.6	Test Environment and Access URL	33
6.6.1	Test Environment	33
6.6.2	Test URL	33

Revision History

Name	Date	Reason for Changes	Version
UTMS Software Project Management Plan	17.12.2025	Draft	0
UTMS Software Project Management Plan	21.12.2025	Submission	1.0
UTMS Software Project Management Plan	07.01.2026	Updated Submission	1.1

1 Overview

The Software Project Management Plan (SPMP) for the Undergraduate Transfer Management System (UTMS) is developed in accordance with IEEE Std. 1058-1998. This document defines the key processes, constraints, and deliverables that govern the planning, execution, and monitoring of the project. It provides a structured approach to project management while supporting the effective preparation and delivery of project management documentation and oversight activities.

SPMP establishes the overall framework and management methodologies required to ensure organized and efficient project execution. By clearly addressing project scope, scheduling, resource allocation, and risk management, the plan serves as a central reference for coordination among the project team, stakeholders, and supervisory bodies, supporting the successful development of the Undergraduate Transfer Management System.

1.1 Purpose, scope, and objectives

Purpose:

The main objective of this SPMP is to document the project management approach for effectively controlling the lifecycle of the Undergraduate Transfer Management System (UTMS) project. It defines project roles and responsibilities, establishes schedules, and outlines risk mitigation measures to support consistent project monitoring, control, and reporting across all phases.

Scope:

This SPMP outlines a formal and systematic approach to managing the UTMS project lifecycle, supported by clearly defined resource, schedule, and budget plans. It specifies the project management deliverables—such as work breakdown structures, timelines, risk logs, and progress reports—and functions as a central reference for coordinating internal activities and communicating project status and deliverables to external stakeholders.

Objectives:

1. Establish standardized project management practices for the development and delivery of the Undergraduate Transfer Management System (UTMS).
2. Ensure that project scope, schedules, and resource allocations are aligned with institutional objectives and constraints.
3. Define clear methodologies and templates to support task assignment, scheduling, and progress monitoring.
4. Improve team coordination by clearly specifying roles, responsibilities, and communication procedures.
5. Provide a customized project management plan that supports the smooth integration of the UTMS with existing institutional systems.

1.2 Assumptions and constraints

Assumptions:

- Undergraduate transfer regulations defined by YÖK and IZTECH remain stable throughout the project lifecycle.
- External systems (ÖSYM, YÖKSİS, and UBYS) are available and accessible for data verification during system operation.
- Administrative units (ÖİDB, YGK, Faculty Boards, and YDYO) actively participate in the digital workflow and perform required reviews within defined timeframes.
- Users (students and staff) possess basic computer literacy and receive adequate guidance or training prior to system deployment.
- Required IT infrastructure, including servers, databases, and network services, is provisioned and maintained by the institution.

Constraints:

- The SPMP must comply with applicable YÖK regulations, institutional policies of IZTECH, and relevant data protection laws (e.g., GDPR / KVKK) governing project documentation and management practices.
- The SPMP defines management support for academic decision-making processes; final academic judgments, including eligibility and course equivalence decisions, remain the responsibility of authorized institutional bodies and are outside the scope of project management automation.
- Project planning and scheduling activities described in the SPMP are dependent on the availability and reliability of external institutional systems (e.g., ÖSYM, YÖKSİS) for coordination and validation; disruptions may affect planned timelines.
- All project management activities governed by the SPMP must adhere to predetermined academic schedules, and no timeline extensions beyond approved milestones are permitted.
- The SPMP scope is limited to managing undergraduate transfer–related project activities; project management for other academic processes or fully automated academic decision-making is excluded.

1.3 Project deliverables

This section presents the dates and submissions (1 for each) to be delivered to project instructors and organization (IZTECH), and explains the definitions for each one.

1. | 8 October - Project Charter Submission

The Project Charter formally authorizes the project and acts as a core reference document that defines its objectives, scope, and key milestones. It outlines the organizational structure, allocates resources, and ensures alignment by securing the required approvals.

2. | 26 October - Problem Analysis Report Submission

This report finds the primary areas of the problems and analyzes the existing AS-IS process in detail, and it presents an improved TO-BE model incorporating automation to enhance efficiency. Additionally, the document outlines current limitations, including Jackson's Context Diagram to clarify the system environment, and specifies the high-level functional requirements of the proposed solution.

3. | 5 November - Updated Problem Analysis Report Submission

After receiving the review feedback, this version of the Problem Analysis submission provides an updated and refined basis for the considered solution approach.

4. | 23 November - SRS Submission

The Software Requirements Specification (SRS) defines the complete set of system requirements, covering functional, non-functional, and technical aspects. SRS details the use case scenarios and acts as the primary reference document guiding the system's design and development.

5. | 3 December - Updated SRS Submission

A reviewed and renewed version for the former SRS submission. It ensures accuracy and alignment with the goals of the project.

6. | 21 December - SPMP Submission

The Software Project Management Plan (SPMP) serves as a structured framework for managing the project, detailing schedules, resource assignments, risk reducing approaches, and project tracking and control mechanisms.

7. | 7 January - Updated SPMP Submission

A renewed version for the previous SPMP submission, to clarify the roadmap for the project execution, based on the review feedback.

8. | 23 March - Design Submission:

The design document presents both high-level and detailed views of the system. It includes architectural diagrams, component definitions, and the underlying design decisions, and functions as a technical blueprint for system implementation.

9. | 1 April – Updated Design Submission

Renewed version for the Design submission regarding the feedback of the review, ensuring it aligns with the requirements and industry standards.

10. | 20 April - Test Report 1st Version Submission

It provides an overview of the implementation, providing details of testing and results. The first version of the test report assesses system functionality by comparing it against the requirements defined in the SRS and the corresponding design documents.

11. | 29 April - Updated Test Report 1st Version Submission

This submission revises the initial test report by incorporating feedback and resolving identified defects, inconsistencies, and opportunities for improvement.

12. | 6 May – 1st Release of the Software System

The initial software release delivers a preliminary testing document that defines test cases, scenarios, and validation methods for system capability. It is intended as an early demo to collect feedback from users.

13. | 1 June - 2nd (Final) Release of the Software System (including Design & Test Report 2nd version)

The final release delivers the fully implemented software system along with updated design documentation and a complete test report. It confirms that all specified requirements have been satisfied, validates system performance, and indicates if it is ready for deployment.

1.4 Schedule and budget summary

Submission	Start Date	End Date	Allocated Budget
Project Charter	08.10.2025	08.10.2025	14.000 TL
Problem Analysis Report	09.10.2025	26.10.2025	252.000 TL
Updated Problem Analysis Report	27.10.2025	05.11.2025	140.000 TL
SRS	06.11.2025	23.11.2025	252.000 TL
Updated SRS	24.11.2025	03.12.2025	140.000 TL
SPMP	04.12.2025	21.12.2025	252.000 TL
Updated SPMP	22.12.2025	07.01.2026	238.000 TL
Design	08.01.2026	23.03.2026	518.000 TL
Updated Design	24.03.2026	01.04.2026	126.000 TL
Test Report 1 st Version	02.04.2026	20.04.2026	525.000 TL
Updated Test Report 1 st Version	21.04.2026	29.04.2026	126.000 TL
1 st Release of the Software System	30.04.2026	06.05.2026	98.000 TL
2 nd (Final) Release of the Software System (Including Design & Test Report 2 nd Version)	07.05.2026	01.06.2026	609.000 TL
			Total: 3.290.000 TL

2 References

Title	Report Number	Date	Author	Path	Publishing Organization
Inter-institutional Horizontal Transfer Guidelines		21.12.2023	ÖİDB	https://ogrencisleri.iyte.edu.tr/wp-content/uploads/sites/99/2023/12/IYTE-Kurumlar-Arasi-Yatay-Geçiş-Yönergesi-21.12.2023.pdf	İYTE
Internal and Inter-institutional Horizontal Transfer Application Documents		X	ÖİDB	https://ogrencisleri.iyte.edu.tr/wp-content/uploads/sites/7/2019/06/Kurum-İç-i-ve-Kurumlar-Arasi-Yatay-Geçiş-Başvuru-Belgeleri.pdf	İYTE
Specific Transfer Requirements for Departments		18.05.2023	ÖİDB	https://ogrencisleri.iyte.edu.tr/wp-content/uploads/sites/99/2023/05/Kurum-İç-i-ve-Kurumlar-Arasi-Yatay-Geçiş-Özel-Şartları-18.05.2023.pdf	İYTE

Project Charter		08.10.2025	Group 12	 G12_ProjectCharter.doc	Group 12
Problem Analysis Report		05.11.2025	Group 12	 G12_ProblemAnalysisReport.pdf	Group 12
SRS		03.12.2025	Group 12	 G12_SRS.pdf	Group 12

3 Definitions

Term	Definition
UTMS	Undergraduate Transfer Management System. A centralized web-based platform developed for IZTECH to digitize and automate the undergraduate transfer process.
SPMP	Software Project Management Plan prepared according to IEEE Std. 1058.
SRS	Software Requirements Specification describing system requirements.
ÖİDB	Registrar's Office responsible for document verification and result publication.
YGK	Departmental Transfer Commission, responsible for academic evaluation and ranking.
YDYO	School of Foreign Languages responsible for English proficiency verification.
YÖK	Council of Higher Education regulating transfer rules in Türkiye.
AS-IS	Current partially manual transfer process.
TO-BE	Future automated transfer process after UTMS implementation.
Applicant	A student who applies for an undergraduate transfer through the UTMS

Use Case (UC)	A description of system behavior that specifies interactions between actors and the system to achieve a goal.
Actor	An external entity (user or system) that interacts with UTMS
API	Application Programming Interface A standardized interface enabling communication between UTMS and external systems such as ÖSYM and YÖKSİS
Work Package (WP)	The smallest, manageable unit of work in a project. It defines a specific set of tasks, deliverables, responsibilities, and time frames, allowing the work to be planned, assigned, monitored, and controlled effectively within the project structure.
Baseline	A fixed reference point for a project (scope, schedule, or cost) that is approved and used to measure performance. Actual progress is compared against the baseline to identify deviations and control changes.
Milestone	a significant checkpoint in a project that marks the completion of a major phase, deliverable, or key event. It has no duration and is used to track progress and decision points.

4 Project context

4.1 Product acceptance plan

The Product Acceptance Plan defines the procedures and objective criteria by which the deliverable work products of the UTMS project shall be evaluated and formally accepted by the acquiring organization.

Acceptance of deliverables shall be based on measurable and verifiable criteria that are agreed upon by representatives of the development organization (Group 12) and the acquiring organization (course supervisor).

Formal acceptance is achieved through documented review approval following inspection, testing, demonstration, and analysis activities.

4.1.1 Acceptance Criteria

For a work product to be considered acceptable, it must meet the following objective criteria:

- **SRS Compliance:** The software must fulfill all functional and non-functional requirements specified in the approved Software Requirements Specification (SRS).

- **Testing Success:** All test cases defined in the Test Report must be executed, and all critical defects must be resolved.
- **Documentation Quality:** All technical documents (Design, SPMP, Test Reports) must follow the required academic templates and incorporate feedback from previous review cycles.
- **Consistency:** The "TO-BE" model proposed in the Problem Analysis Report must be accurately reflected in the final software implementation.

4.1.2 Acceptance Methods

The following methods shall be used to determine acceptability of work products:

- **Testing:** Execution of planned test cases defined in the Test Report, with zero unresolved critical defects.
- **Demonstration:** Live system demonstration during scheduled release milestones to validate functional behavior.
- **Inspection:** Structured review of documents (SRS, SPMP, Design, Test Report) for IEEE format compliance and completeness.
- **Analysis:** Comparison of implemented functionality against SRS requirements using traceability matrices.

Work Product	Acceptance Criteria	Verification Method	Approver
SRS	100% requirements defined & traced	Inspection	Supervisor
SPMP	IEEE 1058 compliance	Inspection	Supervisor
Software	All critical tests passed	Testing & Demo	Supervisor
Final Release	Requirements satisfied	Analysis	Supervisor

4.1.3 Acceptance Process

The acceptance process will follow the incremental delivery schedule:

1. **Preliminary Acceptance:** Following the 1st Release, the system will be evaluated for core functionality and usability.

2. **Final Review:** The final software artifacts, including source code, design blueprints, and defect logs, will be submitted for a final audit.
3. **Formal Handover:** Final acceptance occurs upon the successful "Final Presentation" (01.06.2026) and the formal approval of the project jury.

4.2 Project organization

The Undergraduate Transfer Management System (UTMS) project is executed by **Group 12** within the scope of the CENG 323 course. The project organization is structured to ensure clear responsibility allocation, effective coordination among team members, and controlled interaction with external academic and institutional stakeholders. This section describes the project's external interfaces, internal organizational structure, and the roles and responsibilities of the project team members.

4.2.1 External interfaces

The UTMS project interacts with several organizational entities external to the project team. These interfaces define the organizational boundaries and communication channels required for successful project execution. The course instructor reviews and approves all formal deliverables, while administrative stakeholders provide domain knowledge and validation during analysis and review phases.

- **Parent Organization:**

İzmir Institute of Technology (IZTECH), under which the project is conducted as part of the CENG 323 – Software Project Management course.

- **Acquiring Organization / Academic Authority:**

Course instructor and project supervisor, who act as the primary authority for reviewing, evaluating, and accepting project deliverables.

- **Administrative Stakeholders:**

University administrative units involved in undergraduate transfer processes, including:

- Student Affairs Department (ÖİDB)
- Faculty Boards
- Undergraduate Transfer Committees (YGK)
- School of Foreign Languages (YDYO)


- **External Systems and Data Providers:**

External institutional systems that the UTMS conceptually integrates with for validation and data verification:

- ÖSYM

- YÖKSİS
- UBYS

Communication with external entities is conducted through formal document submissions, review feedback, scheduled demonstrations, and academic coordination channels defined by the course structure.

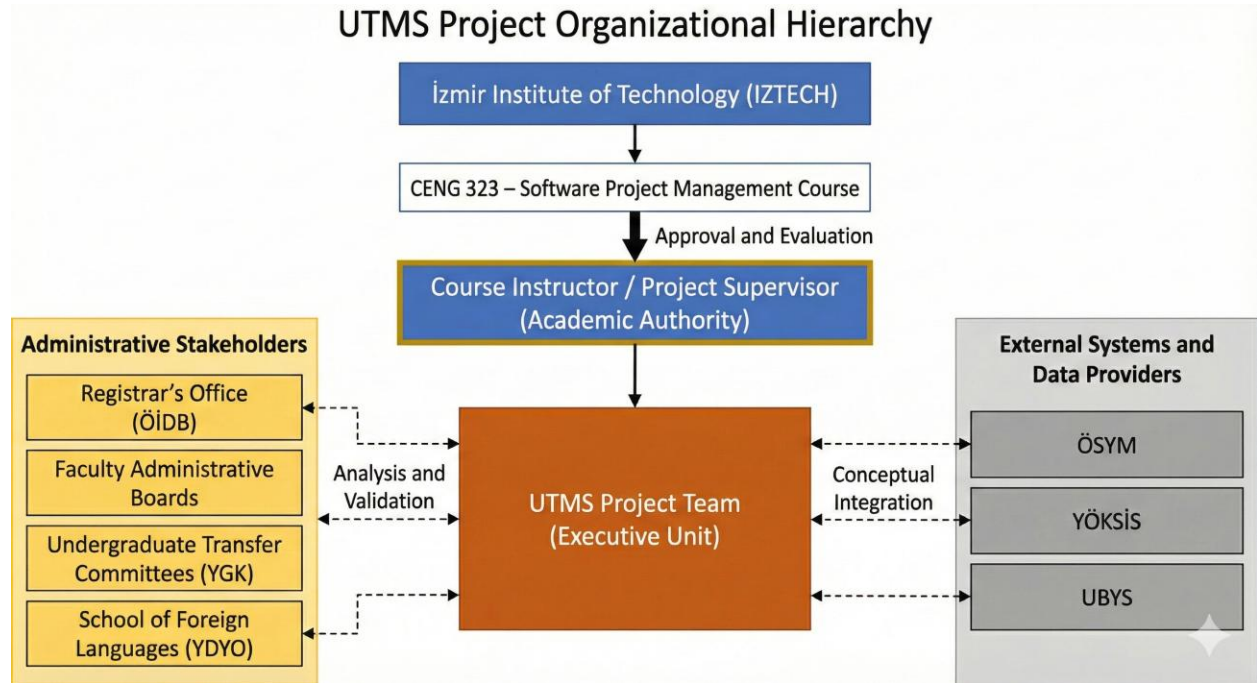

4.2.2 Internal structure


The internal structure of the UTMS project is organized around a **collaborative, role-based team model**. All team members actively participate in multiple project phases while assuming primary responsibility for specific work packages.


Category	Description
Project Coordination	Scheduling, milestone tracking, and progress monitoring are managed by designated team members responsible for project planning and reporting.
Project Management & Planning	Definition of project plans, schedules, resource allocation, and coordination of deliverables.
Problem Analysis & Modeling	Analysis of the current process, development of AS-IS and TO-BE models, and system context definition.
Requirements Engineering	Elicitation, documentation, and validation of functional and non-functional requirements.

Category	Description
System Design	Development of architectural and component-level system designs and documentation of design decisions.
Testing & Validation	Execution of test cases, documentation of results, and verification of compliance with specified requirements.
Release & Deployment	Preparation of software releases, coordination of demonstrations, and delivery of final artifacts.

Supporting processes, including quality assurance, document version control, and review management, are carried out collaboratively across all functional areas. These activities are supported through shared repositories, structured internal reviews, and iterative feedback from project supervisors to ensure consistency, traceability, and quality throughout the project lifecycle.

Lines of authority and communication are maintained through regular internal meetings, documented work packages, and clearly assigned responsibilities for each project activity.

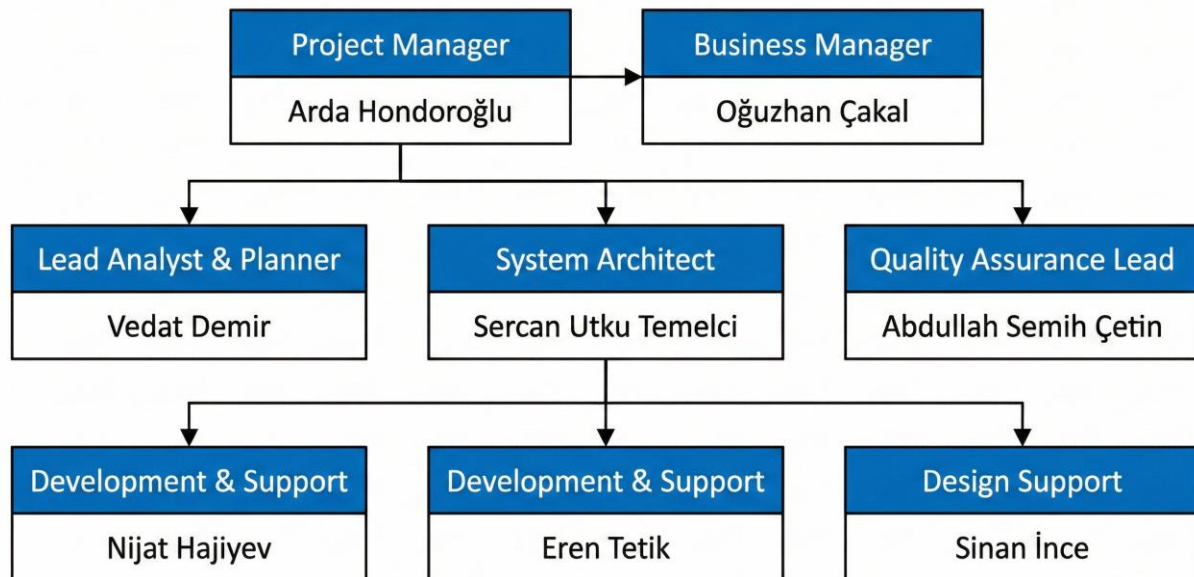

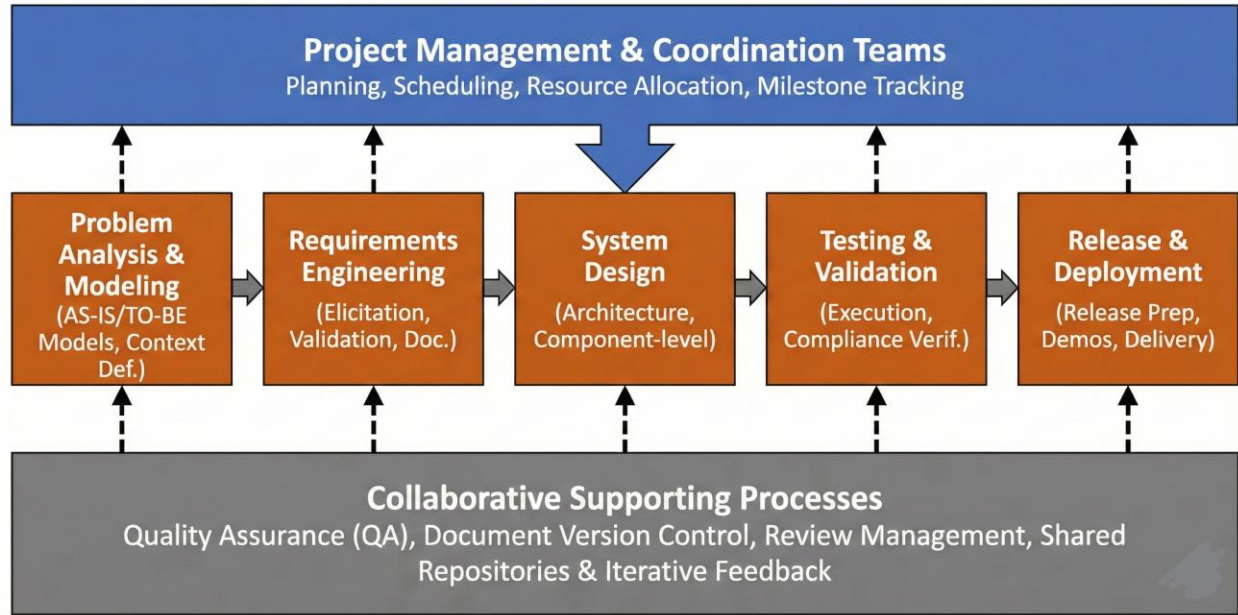

4.2.3 Roles and responsibilities

This section defines the organizational roles assigned to team members. The Project Manager and Business Manager roles are derived directly from the Project Authorization in the Charter. Other technical roles are derived from the Skill Focus areas defined in the SPMP Resource Allocation

Role	Assigned Team Member	Primary Responsibilities
Project Manager	Arda Hondoroğlu	Overall project management, final authorization of deliverables, and risk management.
Business Manager	Oğuzhan Çakal	Project authorization, alignment with business goals, and requirements validation.
Lead Analyst & Planner	Vedat Demir	Analysis of AS-IS/TO-BE processes, schedule planning, and resource tracking.
System Architect	Sercan Utku Temelci	High-level system architecture, component design, and frontend mock-ups.

Role	Assigned Team Member	Primary Responsibilities
Quality Assurance Lead	Abdullah Semih Çetin	Context diagrams, testing execution, defect logging, and SRS compliance.
Development & Support	Nijat Hajiye	Charter development, project roadmap planning, and release management.
Development & Support	Eren Tetik	Administrative approvals, SPMP scheduling, and preliminary testing.
Design Support	Sinan İnce	Organizational structuring and documentation of underlying design decisions.

5 Project planning

This section describes the planning approach for the Undergraduate Transfer Management System (UTMS) project. It defines the work activities, schedule, resource and budget allocations, communication mechanisms, and control procedures required to ensure that the project is executed in a controlled and measurable manner.

5.1 Project work plans

The project work plans define how the UTMS project activities are organized, scheduled, resourced, and monitored. These plans are aligned with the project deliverables and milestones defined in the overall project schedule.

5.1.1 Work activities

The UTMS project is divided into a set of structured work activities following the academic project lifecycle. A Work Breakdown Structure (WBS) is used to decompose the project into manageable work packages. The major work activities include:

- *Project initiation and charter preparation*
- *Problem analysis and AS-IS / TO-BE modelling*
- *Software requirements specification (SRS)*
- *Project management planning (SPMP)*
- *System design (high-level and detailed design)*

- *Implementation and integration*
- *Testing and validation*
- *Deployment preparation and final delivery*

Each work package defines its expected outputs, estimated duration, required resources, acceptance criteria, and dependencies. This level of decomposition enables effective progress tracking and risk identification throughout the project.

WORK PACKAGE TABLE	
WP No: 01	WP Name: Project Charter Development
WP Objective: To formally authorize the project and define its objectives, scope, and key milestones.	
Tasks/Activities to Be Carried Out Within the Scope of the WP: 1.1. Define project objectives and scope. 1.2. Outline organizational structure and allocate resources. 1.3. Secure required approvals. 1.4. Submit Project Charter (08.10.2025).	Responsible Party(ies): 1.1. Lead Analyst 1.2. Design Support 1.3. Quality Assurance Lead 1.4 Project Manager
Success Criteria for the WP: All 5 core sections (Project Objectives, High-Level Scope, Milestone Summary, Budget Estimate, and Risk Register) are completed with no "TBD" (To Be Determined) placeholders.	
Interim Outputs: 1.1. Project Charter Document.	

WORK PACKAGE TABLE	
WP No: 02	WP Name: Problem Analysis & AS-IS/TO-BE Modelling
WP Objective: To analyze the existing process (AS-IS) and present an improved automation model (TO-BE).	
Tasks/Activities to Be Carried Out Within the Scope of the WP: <i>2.1. Identify primary problem areas and analyse the existing AS-IS process.</i> <i>2.2. Create Jackson's Context Diagram to clarify the system environment.</i> 2.3 Identify core system objectives and business constraints.2.4 Create AS-IS and TO-BE reports and eEPC diagrams <i>2.5. Submit Problem Analysis Report (26.10.2025).</i> <i>2.6. Refine the solution approach based on review feedback.</i> <i>2.7. Submit Updated Problem Analysis Report (05.11.2025).</i>	Responsible Party(ies): 2.1 Lead Analyst & Planner 2.2 Quality Assurance Lead 2.3 Developer & Support 2.4 Quality Assurance Lead 2.5 Project Manager 2.6 Business Manager 2.7 Project Manager
Success Criteria for the WP: Process Coverage: 100% of the identified "Problem Areas" (Task 2.1) are addressed in the TO-BE eEPC diagram. Modeling Accuracy: TO-BE model is verified against the AS-IS limitations with 0 logical dead-ends in the eEPC flow. Stakeholder Validation: The "TO-BE" report receives a "Fit-for-Purpose" sign-off from the Business Manager.	
Interim Outputs: <i>2.1. Problem Analysis Report</i> <i>2.2. Jackson's Context Diagram</i> <i>2.3. AS-IS eEPC</i> <i>2.4 TO-BE eEPC</i>	

WORK PACKAGE TABLE	
WP No: 03	WP Name: Software Requirements Specification (SRS)
WP Objective: To define the complete set of system requirements, covering functional, non-functional, and technical aspects.	
Tasks/Activities to Be Carried Out Within the Scope of the WP: 3.1. <i>Detail the use case scenarios.</i> 3.2. <i>Decompose business objectives into detailed functional and non-functional specifications.</i> 3.3 <i>Create mock-ups of frontend.</i> 3.4. <i>Submit SRS (23.11.2025).</i> 3.5. <i>Review feedback and align requirements with project goals.</i> 3.6. <i>Submit Updated SRS (03.12.2025).</i>	Responsible Party(ies): 3.1. System Architect 3.2. Quality Assurance Lead 3.3. Quality Assurance Lead 3.4. Project Manager 3.5. Lead Analyst & Planner 3.6. Project Manager
Success Criteria for the WP: Traceability: 100% of high-level objectives from WP-02 Task 2.3 are mapped to at least one functional requirement in the SRS. Testability: 100% of requirements are written as "testable" statements (avoiding vague words like "easy to use" or "fast"). Completeness: SRS includes a full Use Case Diagram with 0 orphaned use cases (every use case must have an actor and a description).	
Interim Outputs: 3.1. <i>Software Requirements Specification (SRS) Document.</i> 3.2. <i>Frontend Mock-ups</i> 3.3. <i>Use case Scenarios</i>	

WORK PACKAGE TABLE	
WP No: 04	WP Name: Software Project Management Plan (SPMP)
WP Objective: To establish a structured framework for project management, including resource scheduling, tracking mechanisms, and explicit mitigation strategies for identified technical and regulatory risks.	
Tasks/Activities to Be Carried Out Within the Scope of the WP: 4.1. Define schedules, resource assignments, and tracking mechanisms. 4.2. Develop a Risk Register and Mitigation Plan addressing regulatory constraints, external dependencies, and workflow bottlenecks. 4.3. Submit SPMP (21.12.2025). 4.4. Clarify the roadmap for project execution based on review feedback. 4.5. Submit Updated SPMP (07.01.2026).	Responsible Party(ies): 4.1 System Architect 4.2 Project Manager 4.3 Project Manager 4.4 Lead Analyst & Planner 4.5 Project Manager
Success Criteria for the WP: A comprehensive plan detailing the project execution roadmap is established. Changes in review report corrected.	
Interim Outputs: 4.1. SPMP Document 4.2. Work Packages 4.3. Work Schedule	

WORK PACKAGE TABLE	
WP No: 05	WP Name: Architectural & Component Design
WP Objective: To present both high-level and detailed views of the system to serve as a technical blueprint.	
Tasks/Activities to Be Carried Out Within the Scope of the WP: 5.1. <i>Create architectural diagrams and component definitions.</i> 5.2. <i>Define System Boundaries: Categorize every component as Automated, Semi-Automated, or Manual interface based on the TO-BE model.</i> 5.3. <i>Submit Design Document (23.03.2026).</i> 5.4. <i>Renew design submission based on feedback to align with industry standards.</i> 5.5. <i>Submit Updated Design Document (01.04.2026).</i>	Responsible Party(ies): 5.1. System Architect 5.2. Development & Support 5.3. Project Manager 5.4. Business Manager 5.5. Project Manager
Success Criteria for the WP: Design specifications are complete and ready for implementation. Changes in review report corrected.	
Interim Outputs: 5.1. <i>Design Document</i> 5.2. <i>Architectural Diagrams</i>	

WORK PACKAGE TABLE	
WP No: 07	WP Name: Software Release & Deployment
WP Objective: To deliver the fully implemented software system, validated for performance and readiness for deployment.	
Tasks/Activities to Be Carried Out Within the Scope of the WP: 7.1. Prepare preliminary testing document and test cases. 7.2. Deliver 1st Release of the Software System for user feedback (06.05.2026). 7.3. Finalize implementation and update design documentation. 7.4. Deliver 2nd (Final) Release of the Software System (01.06.2026).	Responsible Party(ies): 7.1. Development & Support 7.2. Project Manager 7.3. Business Manager 7.4 Project Manager
Success Criteria for the WP: Final software is released, all requirements are satisfied, and the system is ready for deployment. Changes in review report are corrected	
Interim Outputs: 7.1. 1st Software Release 7.2. Final Software Release 7.3. User Manuals	

5.1.2 Schedule Allocation


This subclause depicts the time-sequencing constraints and schedule relationships among the project work activities. The schedule is driven by the submission deadlines outlined in the Project Deliverables section

ID	Task Name	Start	End	Duration	Predecessors
WP 01	Project Charter Development	08.10.2025	08.10.2025	1 Day	-
1.1	Define objectives and scope	08.10.2025	08.10.2025	1 Day	-
1.2	Outline organizational structure	08.10.2025	08.10.2025	1 Day	-
1.3	Secure required approvals	08.10.2025	08.10.2025	1 Day	-
1.4	Milestone: Project Charter Submission	08.10.2025	08.10.2025	0 Days	1.1, 1.2, 1.3
WP 02	Problem Analysis & Modelling	09.10.2025	05.11.2025	28 Days	WP 01
2.1	Identify problem areas & Analyse AS-IS	09.10.2025	15.10.2025	7 Days	WP 01
2.2	Create Jackson's Context Diagram	16.10.2025	18.10.2025	3 Days	2.1
2.3	Specify high-level requirements	19.10.2025	21.10.2025	3 Days	2.2
2.4	Create AS-IS and TO-BE eEPC diagrams	22.10.2025	25.10.2025	4 Days	2.3
2.5	Milestone: Problem Analysis Report	26.10.2025	26.10.2025	0 Days	2.4
2.6	Refine solution based on feedback	27.10.2025	04.11.2025	9 Days	2.5
2.7	Milestone: Updated Problem Analysis	05.11.2025	05.11.2025	0 Days	2.6

ID	Task Name	Start	End	Duration	Predecessors
WP 03	Software Requirements (SRS)	06.11.2025	03.12.2025	28 Days	WP 02
3.1	Detail Use Case Scenarios	06.11.2025	12.11.2025	7 Days	WP 02
3.2	Define functional/non-func. requirements	13.11.2025	18.11.2025	6 Days	3.1
3.3	Create Frontend Mock-ups	19.11.2025	22.11.2025	4 Days	3.2
3.4	Milestone: SRS Submission	23.11.2025	23.11.2025	0 Days	3.3
3.5	Review feedback & align requirements	24.11.2025	02.12.2025	9 Days	3.4
3.6	Milestone: Updated SRS Submission	03.12.2025	03.12.2025	0 Days	3.5
WP 04	Project Planning (SPMP)	04.12.2025	07.01.2026	35 Days	WP 03
4.1	Define schedules & resource assignments	04.12.2025	17.12.2025	14 Days	WP 03
4.2	Milestone: SPMP Submission	21.12.2025	21.12.2025	0 Days	4.1
4.3	Clarify roadmap based on feedback	22.12.2025	06.01.2026	16 Days	4.2
4.4	Milestone: Updated SPMP Submission	07.01.2026	07.01.2026	0 Days	4.3
WP 05	Architectural & Component Design	08.01.2026	01.04.2026	84 Days	WP 04
5.1	Create architectural diagrams	08.01.2026	15.02.2026	39 Days	WP 04

ID	Task Name	Start	End	Duration	Predecessors
5.2	Document underlying design decisions	16.02.2026	22.03.2026	35 Days	5.1
5.3	Milestone: Design Submission	23.03.2026	23.03.2026	0 Days	5.2
5.4	Renew design based on feedback	24.03.2026	31.03.2026	8 Days	5.3
5.5	Milestone: Updated Design Submission	01.04.2026	01.04.2026	0 Days	5.4
WP 06	System Testing & Reporting	02.04.2026	29.04.2026	28 Days	WP 05
6.1	Execute tests and gather results	02.04.2026	19.04.2026	18 Days	WP 05
6.2	Milestone: Test Report 1st Version	20.04.2026	20.04.2026	0 Days	6.1
6.3	Resolve identified defects	21.04.2026	28.04.2026	8 Days	6.2
6.4	Milestone: Updated Test Report	29.04.2026	29.04.2026	0 Days	6.3
WP 07	Software Release & Deployment	30.04.2026	01.06.2026	33 Days	WP 06
7.1	Prepare preliminary testing docs	30.04.2026	05.05.2026	6 Days	WP 06
7.2	Milestone: 1st Release of Software	06.05.2026	06.05.2026	0 Days	7.1
7.3	Finalize implementation & user manuals	06.05.2026	31.05.2026	26 Days	7.2

ID	Task Name	Start	End	Duration	Predecessors
7.4	Milestone: 2nd (Final) Release	01.06.2026	01.06.2026	0 Days	7.3

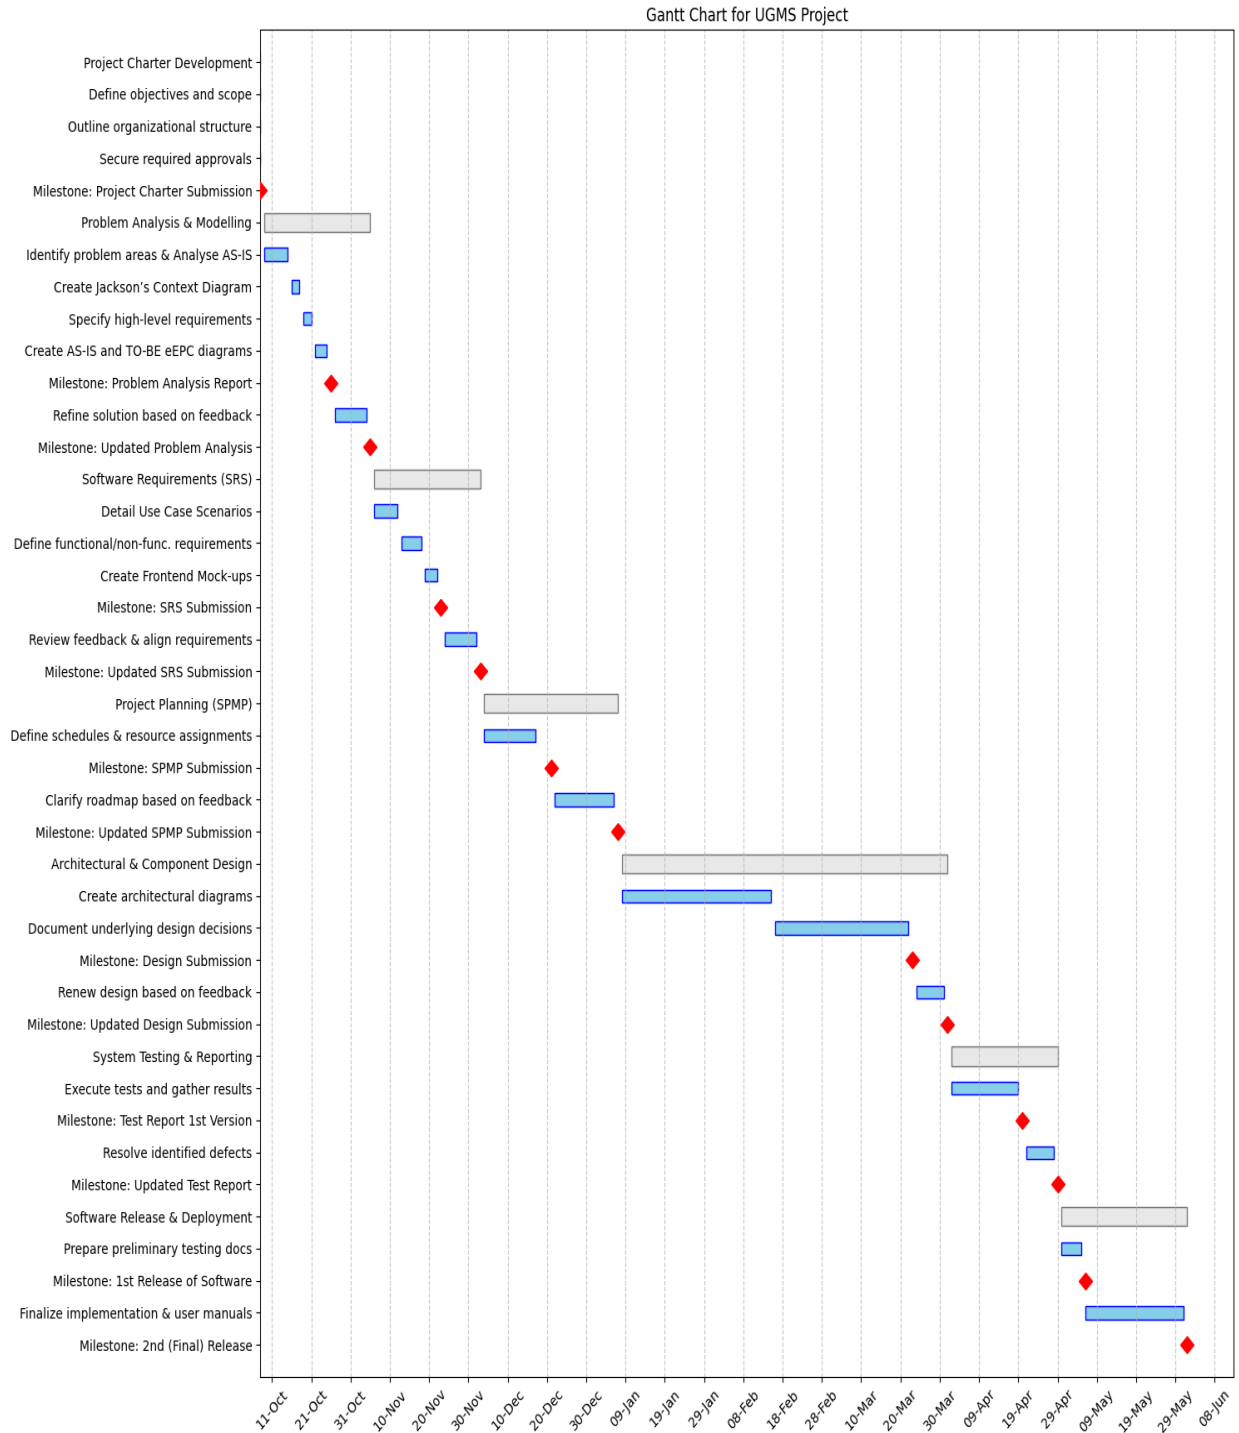

5.1.3 Resource allocation

This section details the personnel resources allocated to each major work package. The allocation is based on the responsibilities defined in the Work Package descriptions.

WP No	Work Package Name	Responsible Personnel	Role / Skill Focus	Est. Effort (Hours)	Timeline
WP 01	Project Charter Development	Nijat Hacıyev, Sinan İnce, Eren Tetik	PM, Planning	40 hrs	Week 1-2
WP 02	Problem Analysis & Modelling	Vedat Demir, A. Semih Çetin, Arda Hondoroğlu	Analysis, Context Diagrams	80 hrs	Week 2-4
WP 03	Software Requirements (SRS)	Oğuzhan Çakal, A. Semih Çetin, S. Utku Temelci	Use Cases, Mock-ups	120 hrs	Week 3-6
WP 04	Project Planning (SPMP)	Vedat Demir, Eren Tetik, Nijat Hacıyev	Scheduling, Roadmap	60 hrs	Week 1-3
WP 05	Architectural Design	S. Utku Temelci, Sinan İnce, Arda Hondoroğlu	Architecture, Decisions	100 hrs	Week 5-8
WP 06	System Testing & Reporting	A. Semih Çetin, Oğuzhan Çakal, Vedat Demir	Testing, Defect Resolution	150 hrs	Week 10-14

WP No	Work Package Name	Responsible Personnel	Role / Skill Focus	Est. Effort (Hours)	Timeline
WP 07	Software Release	Arda Hondoroğlu, Oğuzhan Çakal, S. Utku Temelci	Deployment, Release Management	40 hrs	Week 15-16

5.1.4 Budget allocation

Although the project does not involve external financial expenditure, budget allocation is defined in terms of personnel effort cost.

Effort-based budgeting ensures consistency between planned resource allocation and reported project cost.

Cost Category	Resource Type	Estimated Cost	Notes
Personnel	Development Team (8 Members)	400.000 TL/month	Academic Coursework/ Student Project
Hardware	Personal Laptops / Servers	20.000 TL/month	Provided by students/institution
Software	Development Tools / IDEs	0.00 TL	Open Source / Academic License
Miscellaneous	Printing / Administrative	1000 TL/month	Minimal costs expected
Total		421.000 TL/month	

5.1.5 Communications plan

The communications plan outlines the methods used to engage stakeholders and ensure timely information flow, regarding project status and deliverables

Communication Type	Frequency	Participants	Medium	Goal / Output
Internal Weekly Meeting	Weekly	Group 12 Members	In-person / Discord	Progress tracking, task assignment
Milestone Review	Per Schedule	Group 12, Supervisor	Document Submission	Feedback on deliverables (SRS, SPMP, etc.)
Release Demo	06.05.2026	Group 12, Users/Stakeholders	Software Demo	User feedback collection
Final Presentation	01.06.2026	Group 12, Jury/Supervisor	Presentation	Final project defense & acceptance

5.2 Project assessment and control

This section specifies the metrics and procedures used to measure, report, and control the project schedule and budget.

5.2.1 Schedule control plan

Schedule control is maintained through the monitoring of major milestones defined in the Project Deliverables section.

- **Milestone Tracking:** Achievement of schedule milestones is assessed using objective indicators, such as the submission of the "Project Charter," "SRS," and "Design Document" by their respective deadlines.
- **Corrective Action:** If a delay occurs (e.g., dependency on external APIs like ÖSYM/YÖKSİS causes disruption), the Project Manager will revise the schedule and resource allocation in the "Updated" version of the relevant deliverable (e.g., Updated SPMP)

5.2.2 Budget control plan

Since the project budget is defined in terms of personnel effort costs and academic resource allocation, budget control is managed through Effort-Based Cost Tracking.

- **Cost Performance Monitoring:** The estimated monthly personnel cost of **400,000 TL** is derived from the total effort of the 8-member team. The Project Manager tracks actual "Person-Hours" spent per Work Package. Any significant deviation in hours is recorded as a cost variance.
- **Resource Expense Control:** Although hardware (20,000 TL/month) is provided by the team/institution, its utilization is monitored to ensure no additional administrative or printing costs (estimated at 1,000 TL/month) exceed the project's minimal cash threshold.
- **Reporting & Correction:** Weekly effort reports are translated into "TL equivalent" to verify project health. If a Work Package requires more hours than planned, it is flagged as an "Over-Budget" risk, and tasks are redistributed among the "Responsible Parties" to maintain the 421,000 TL/month efficiency target.

6 Product delivery

The Undergraduate Transfer Management System (UTMS) will be delivered in accordance with the academic project milestones defined in the project schedule. The delivery process ensures that all required software artifacts and documentation are transferred to the acquiring organization in a complete and verifiable manner.

6.1 Delivery Approach

The UTMS will be delivered using an **incremental delivery strategy**, consisting of two main software releases:

- **1st Release (06.05.2026):**
A functional prototype deployed in a test environment, intended for demonstration, usability evaluation, and early feedback.
- **2nd (Final) Release (01.06.2026):**
The fully implemented system that satisfies all approved requirements in the Software Requirements Specification (SRS) and incorporates feedback from the first release.

Each release is subject to review before acceptance. Each delivery milestone shall be evaluated based on functional completeness, compliance with the approved SRS, and successful execution of planned test cases.

6.2 Information Flow During Delivery

- **Internal Information Flow:**

Managed through weekly internal meetings and a Git-based version control system (GitHub) used for source code management, documentation, and issue tracking.

- **External Information Flow:**

Managed through:

- Formal document submissions (PDF)
- Review feedback from the course instructor
- Scheduled live demonstrations during release milestones

All feedback received during delivery milestones will be documented and tracked until resolution.

6.3 Packaging and Delivery Method

The UTMS and its related artifacts will be packaged and delivered in the following manner:

6.3.1 Software Delivery

- Web-based application deployed on a test server
- Platform-independent access via browser
- No client-side installation required

6.3.2 Source Code Delivery

- Delivered via a version-controlled repository
- Includes:
 - Source code
 - Configuration files
 - Deployment instructions

6.3.3 Documentation Delivery

All documentation will be delivered in **PDF format**, following academic templates required by the course.

The following artifacts will be delivered at the Final Release stage:

Artifact	Format	Description
Undergraduate Transfer Management System	Web Application	Fully implemented and deployable system

Software Requirements Specification (Final)	PDF	Approved requirements baseline
Software Project Management Plan (Final)	PDF	Project execution and control documentation
Design Document (Final)	PDF	Architectural and component design
Test Report (Final)	PDF	Test cases, results, and defect resolution
User Manual	PDF	System usage instructions
Source Code	Repository	Version-controlled source and configs

6.4 Delivered Artifacts

The final delivery includes:

- Fully implemented Undergraduate Transfer Management System
- Final Design Document
- Final Test Report
- User documentation describing system usage and workflows
- Source code and configuration files necessary for system deployment.

6.5 Acceptance and Handover

Acceptance of UTMS is based on the following conditions:

- Successful execution of all critical test cases defined in the Test Report
- Compliance with all functional and non-functional requirements specified in the SRS
- Completion of required documentation with incorporated review feedback
- Successful live demonstration during the **Final Presentation (01.06.2026)**

Upon approval by the course instructor and project supervisors, the final software release and all associated artifacts will be formally handed over, completing the project delivery process.

6.6 Test Environment and Access URL

6.6.1 Test Environment

All system tests and demonstrations will be conducted in a **dedicated web-based test environment**, separated from any production-level system.

- The system will run as a **web application**
- No local installation will be required
- Access will be provided through standard modern web browsers (Chrome, Firefox, Edge)

6.6.2 Test URL

The system will be tested and demonstrated via a publicly accessible test URL provided by the project team.

- **Test Environment URL:**
<https://utms-test.group12.edu.tr> (*example – final URL will be announced before release*)
- **Final Release URL:**
<https://utms.group12.edu.tr> (*academic deployment environment*)

Access credentials (test user accounts for students and administrators) will be provided to the course instructor and reviewers prior to demonstrations.
